

Denta Properties & Infrastructures Pvt Ltd

Name of the Project: "Construction of Lift Irrigation Scheme to Gobbarakal, Somalapur and Rowdakund villages in Sindhanur taluk of Raichur District".

Awarded To : *Veerayya Hiremath by Irrigation Department, GOK.*

Executed By: *M/s. Denta Properties & Infrastructures Pvt Ltd.*

PROJECT DETAILS


- ▶ Date of Agreement : 12th May, 2022
- ▶ Date of Commencement : 13th May, 2022
- ▶ Project Completion Date : 11th Jul, 2023

- ▶ Agreement Value :
- ▶ Value of Work done
as on 31/05/23 :


Scope of work

- ▶ No. of Lifting Stations : 1 nos
- ▶ Sources Location : Tungabhadra Water
- ▶ Total Length of Pipeline : 12.00Km (Mild Steel)
- ▶ Construction of 11KV Sub stations near by pump house with Transmission line connecting by existing sub station to pump house substation.

Present Status of work

- Survey Status : Survey completed for Pipeline network.
 - Submission of Designs : Raising Main, 1 PH GAD & Structural completed.
 - Approval of Designs : Raising Main, 1 PH GAD completed, Structural completed.
 - Grounding of Work : Started In the Month of May 2022. Work is in progress pumping station and pipe laying.
- 

Work Progress Photos

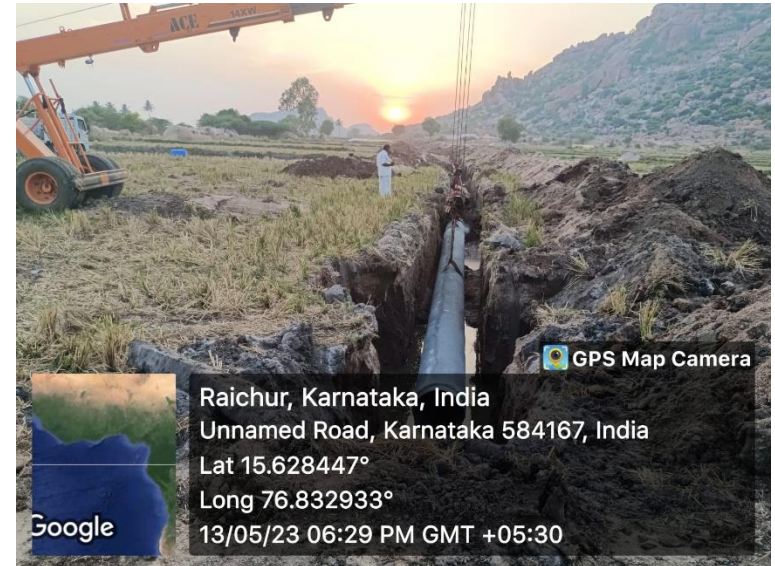

A scenic view of a rocky coastline. The foreground shows a sandy, light-colored rock formation with sparse green vegetation. The middle ground is a calm, blue-grey body of water extending to the horizon. The sky is a pale, clear blue. The text "Thank You" is overlaid in the center in a blue, italicized serif font.

Thank You
